

304 of 780

Work Order ID 131724

Tuesday, April 21, 2015 1:47:56 PM

131724

Page 1

Item ID: D5152-5 Accept *N900040100* Setup Start *NS1*

Revision ID:

Item Name: Fwd Step Post Stop *NS2*

Start Date: 4/20/15 Start Qty: 10.00 *10* Cust Item ID:

Required Date: 4/20/15 Req'd Qty: 10.00 *10* Customer:

Reference:

Approvals: Process Plan: MCS Date: 1504-23 Tooling: _____ Date: _____ Run Start *NR1*

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D5152	B

100

100

Doosan

Doosan Lathe

DOOSAN LATHE

Memo

1- Turn as per Folio FB

Rev: WA &Dwg Rev: B

0.00

0.00

DAS
25
9-89

15-4-25

110

110

QC

Quality Control

QC2- Inspect parts off machine FAI/FAIB

Memo

0.00

0.00

DAS
25
9-89

15-4-25

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS <table style="width: 100%; border: none;"> <tr> <td style="width: 15%;">Skid-tube ☐</td> <td style="width: 15%;">Cross tube ☐</td> <td style="width: 15%;">Water Jet ☐</td> <td style="width: 15%;">Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>						Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐																						
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																						
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																						
Large Fab ☐	Composite ☐	Supplier ☐																							
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval																		
Description Work Order Deviation				Disposition				Completed By																	
								Lead hand / Supervisor Approval Verification																	
								QC / QA Coordinator Approval																	
Root Cause		FAULT CATEGORY																							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐																				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐																				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐																				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐																				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐																				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐																				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐																				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐																				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐																				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐																				
Past Expiry Date ☐	Manufacturing Process ☐																								
Misidentified ☐	Past Due ☐	OTHER :																							

Work Order ID 131724

131724

Page 2

Tuesday, April 21, 2015 1:47:56 PM

Item ID: D5152-5 Accept *N900040100* Setup Start *NS1*
 Revision ID: Stop *NS2*
 Item Name: Fwd Step Post
 Start Date: 4/20/15 Start Qty: 10.00 *10* Cust Item ID:
 Required Date: 4/20/15 Req'd Qty: 10.00 *10* Customer:
 Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start *NR1*
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
120	QC8- Inspect parts - second check	0.00				10	Ø		DAS 44 9-89 15/04/25
120									
QC	Memo	0.00							
Quality Control									
150	Identify as per dwg & Stock Location: <u>WU</u>	0.00				10X			DAS 26 9-89 APR 29 2015
150									
Packaging	Memo	0.00							
Packaging									
170	QC21- Final Inspection - Work Order Release	0.00							
170									
QC	Memo	0.00				MLJ			APR 29 2015
Quality Control									

MLJ APR 29 2015

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	☐ No Re-verification	☐ Pressure/Forced	☐ Temperature/Cure	☐ Power Loss/Surge	☐ Positioned Wrong				
Design ☐	☐ Operator	☐ Bending	☐ Set-up	☐ Folio/Program	☐ Outside Dimensions				
Doc/Data ☐	☐ Offset/Setup	☐ Centre Not Concentric	☐ BOM/Route	☐ Grain	☐ Over/Under tolerance				
Equip/Tooling ☐	☐ Supplier	☐ Cracks	☐ Broken/Damage/Defect	☐ Weld	☐ Part Incorrect				
Handling/Pre ☐	☐ Training	☐ Crimp/Kink/Ripple/Wave	☐ Inspection Incomplete/Unqualified	☐ Wrong Stock Pulled	☐ Part Lost/Missing				
Material ☐	☐ Use for Testing	☐ Cuffs	☐ Contamination	☐ Out of Sequence	☐ Part Moved				
Internal Transport ☐	☐ Poor Information	☐ Crushing	☐ Countersink	☐ Off-set	☐ Drawing				
Tribal Knowledge ☐	☐ Rushing	☐ Heat Treat	☐ Cut Too Short	☐ Mislabeled	☐ Finish				
LOA ☐	☐ Product Improvement	☐ Wave/Twist in Tube	☐ Instructions Incomplete/Unclear	☐ Fit/Function	☐ Misread				
Substation ☐	☐ Process Improvement	☐ Marks/Chatter	☐ Drill Holes	☐ Misaligned/off center	☐ Turning Sequence				
Past Expiry Date ☐	☐ Manufacturing Process	OTHER :							
Misidentified ☐	☐ Past Due								

Picklist Print

Tuesday, April 21, 2015 1:47:56 PM

Page 1

Work Order ID: 131724

131724

Parent Item: D5152-5

D5152-5

Parent Item Name: Fwd Step Post

Start Date: 4/20/15

Required Date: 4/20/15

Start Qty: 10.00

Required Qty: 10.00

Comments: IPP REV:A NEW ISSUE 15-01-08 JLM VERIFIED BY:DD

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
M304RO.750		Purchased		No			f	58.6130		0.263158			

M304RO 750

304 SS Roundbar .750

215-4-25

Location

Loc Qty

Loc Code

MAT029

58.613

M128005

11.25

M128496

47.363

x 38

DQA: _____ Date: _____




WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS <table style="width: 100%; border: none;"> <tr> <td style="width: 15%;">Skid-tube ☐</td> <td style="width: 15%;">Cross tube ☐</td> <td style="width: 15%;">Water Jet ☐</td> <td style="width: 15%;">Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>						Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐																						
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																						
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																						
Large Fab ☐	Composite ☐	Supplier ☐																							
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval																		
Description Work Order Deviation				Disposition				Completed By																	
								Lead hand / Supervisor Approval Verification																	
								QC / QA Coordinator Approval																	
Root Cause		FAULT CATEGORY																							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐																				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐																				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐																				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐																				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐																				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐																				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐																				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐																				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐																				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐																				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____																							
Misidentified ☐	Past Due ☐																								

ITEM	QTY	P/N	DESCRIPTION
	X	D5152-041	FWD POST MOUNT ASSY
1	1	D5152-1	FWD POST MOUNT
2	1	D5152-5	FWD STEP POST

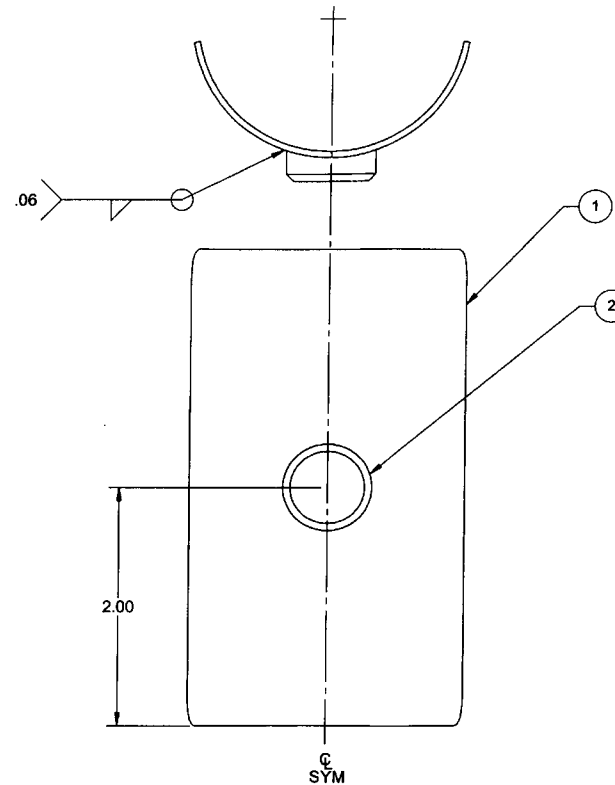

D5152-041 FWD POST MOUNT ASSEMBLY

SHOW
REF TO
BENCH
UNCONTROLLED
SUBJECT TO
WITH
WORK ORDER

NO 131724.MCS
15-04-23

RELEASED

2015 FEB 09


ECN 15-516 4P

- NOTES:
- 1) MATERIAL: N/A
 - 2) FINISH: PRIME PER DART QSI 005 4.2
 - 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
 - 4) UNITS: INCHES UNLESS OTHERWISE NOTED
 - 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
 - 6) IDENTIFICATION: IDENTIFY PER DART QSI 044 6.1
 - 7) WEIGHT: D5152-041= 0.21 lbs

APPROVED

B	COMPLETE REDESIGN, SEE PREVIOUS REV FOR DETAILS	DB	15.01.09
A	NEW ISSUE	DB	14.09.03
REV.	DESCRIPTION	BY	DATE
DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	EPDMA		
CHECKED	DB	DRAWING NO.	REV. B
MFG. APPR.	DD	D5152	SHEET 1 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

ITEM	QTY -043	P/N	DESCRIPTION
	X	D5152-043	AFT POST MOUNT ASSY
1	1	D5152-3	AFT POST MOUNT
2	1	D5152-7	AFT STEP POST

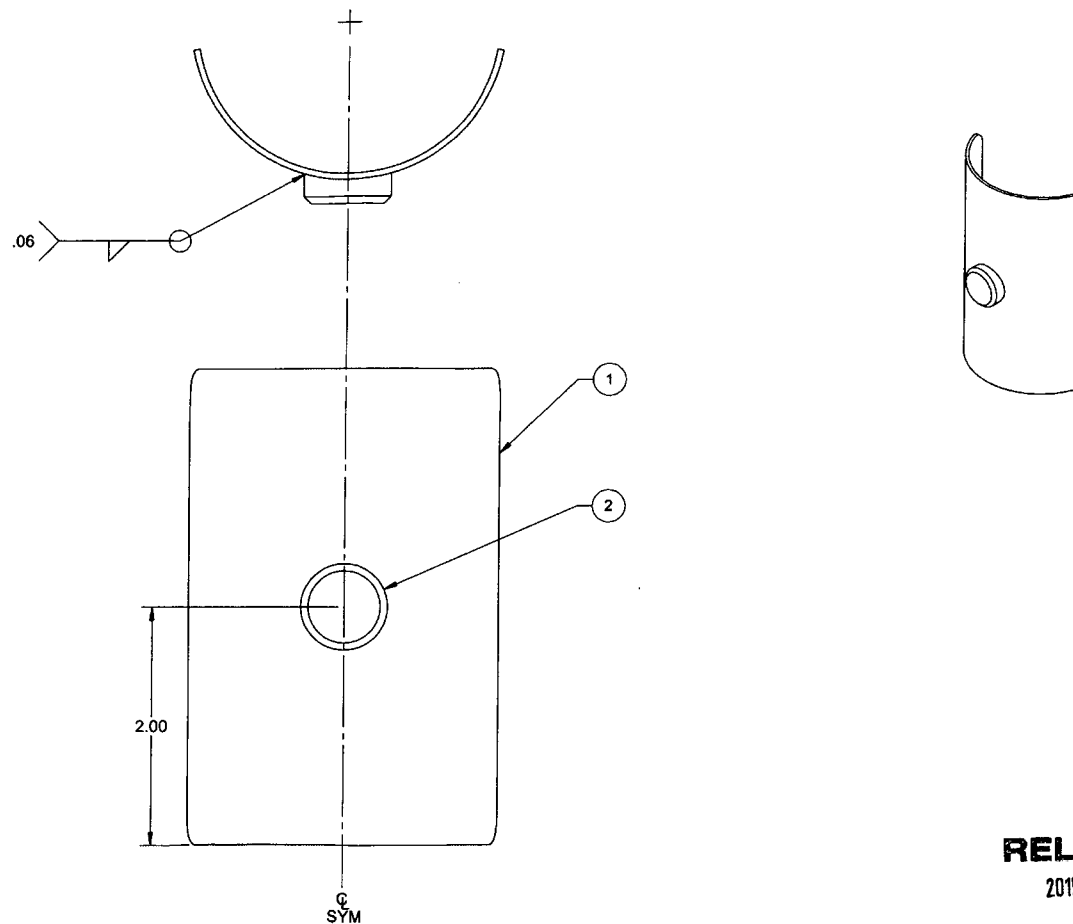

D5152-043 AFT POST MOUNT ASSEMBLY

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: PRIME PER DART QSI 005 4.2
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY PER DART QSI 044 6.1
- 7) WEIGHT: D5152-043= 0.23 lbs


RELEASED

2015 FEB 09


APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	EPDMA	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. B
MFG. APPR.	DD	D5152	SHEET 2 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

8 7 6 5 4 3 2 1

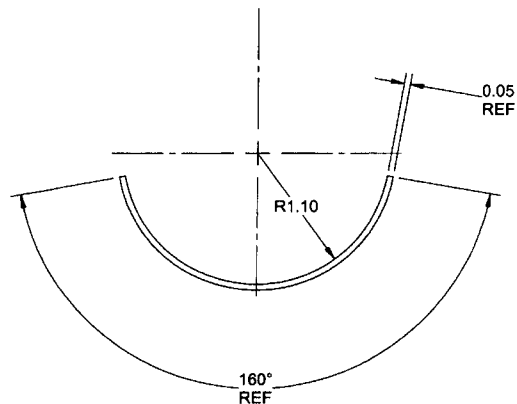

D5152-1 FWD POST MOUNT
(MAKE FROM D5152-1F)

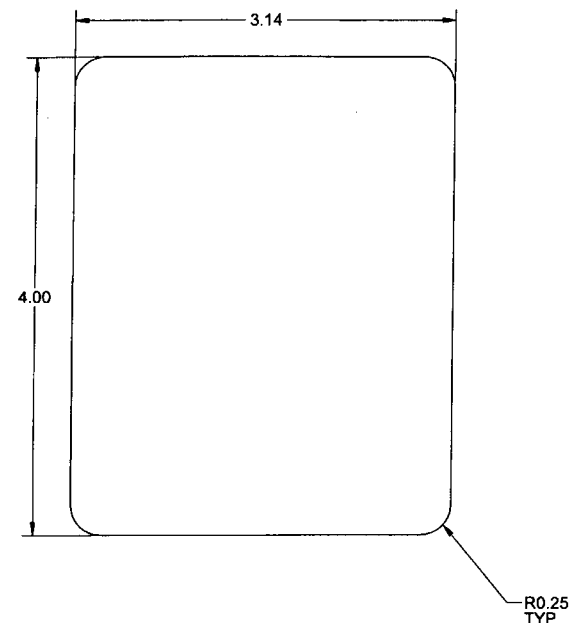

D5152-1F FWD POST MOUNT
(FLAT PATTERN)

RELEASED


2015 FEB 09

NOTES:


- 1) MATERIAL: AISI 304/316 STAINLESS STEEL SHEET PER MIL-S-5059 OR AMS 5513 OR 5524 OR ASTM A240 OR ASME SA240, 0.050" THICK (PER DART SPEC M304S18GA)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: N/A

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	EPDMA	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. B
MFG. APPR.	DD	D5152	SHEET 3 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

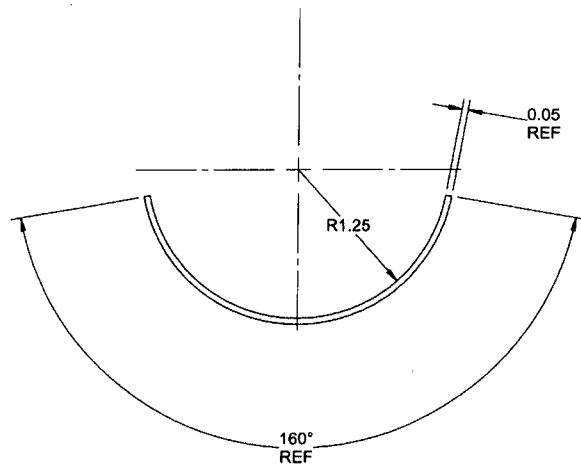

D5152-3 AFT POST MOUNT
(MAKE FROM D5152-3F)

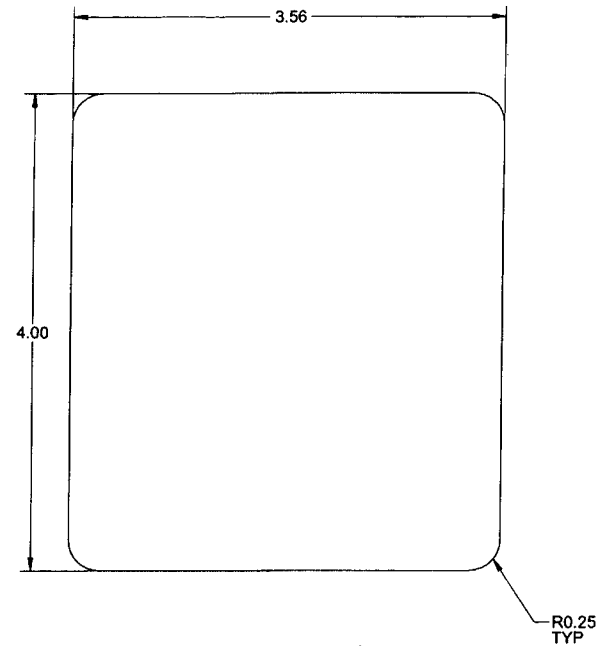

D5152-3F AFT POST MOUNT
(FLAT PATTERN)

RELEASED

2015 FEB 09

NOTES:

- 1) MATERIAL: AISI 304/316 STAINLESS STEEL SHEET PER MIL-S-5059 OR AMS 5513 OR 5524 OR ASTM A240 OR ASME SA240, 0.050" THICK (PER DART SPEC M304S18GA)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: N/A

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	EPDMA	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. B
MFG. APPR.	DD	D5152	SHEET 4 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

8 7 6 5 4 3 2 1

D

D

C

C

B

B

A

A

R1.150

R1.300

0.20

0.20

0.06 X 45° CMF

0.06 X 45° CMF

Ø0.725

Ø0.725

D5152-5 FWD STEP POST

D5152-7 AFT STEP POST

RELEASED

2015 FEB 09

NOTES:

- 1) MATERIAL: AISI 304/316 SS ROUND BAR PER ASTM A276, REF DART SPEC M304R0.750
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.02 lbs

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	EPDMA	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. B
MFG. APPR.	DD	D5152	SHEET 5 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

8 7 6 5 4 3 2 1

